

North Pacific Fishery Management Council

Agenda #12, Jan. 1978

Harold E. Lokken, Chairman
Jim H. Branson, Executive Director

Mailing Address: P.O. Box 3136DT
Anchorage, Alaska 99510

Suite 32, 333 West 4th Avenue
Post Office Mall Building




Telephone: (907) 274-4563
FTS 265-5435

MEMORANDUM

DATE: January 20, 1978

TO: Council Members, AP Members and SSC Members

FROM: Jim H. Branson 

SUBJECT: Cycle of Management Plan Development

I have redrafted the 'Cycle of Management Plan Development' submitted to the Council as an SSC recommendation at the December meeting. There are no substantive changes in that flow-chart, except for the addition of more details and the approximate time period involved (Column 1).

The estimated time to develop a plan from the point when the Council decides on the need to implementation by the Secretary is estimated at 345 to 360 days. Some of these steps can be shortened, but only at the expense of thoroughness.

The first 30 days could conceivably be consolidated into one meeting if the SSC and Advisory Panel makes recommendations for a planning development team (PDT), the Council approves them and gives the PDT its instructions all at the same meeting.


The second time period (day 30 to 90) could conceivably be compressed to 30 days, though experience to date with drafting plans indicates that 60 days is really minimal. The rest of the period until day 210 is minimal as shown, no possibility of cutting the time.

Day 210 to day 240 is a new step. For the previous plans the Council has approved a plan (with revisions considered appropriate based on the public comment period and any other new information available to the Council), the staff and PDT have redrafted, printed and sent the plan forward to the Secretary without another review by the SSC, AP and Council. Under the proposed schedule the Council group would review the plan to be sure it complied with their instructions, after the editorial rewrite and printing, before sending it to the Secretary as their recommendation.

Days after 240 are out of the Council's hands. Its possible for the Secretary to shorten the 60 day review period, but unlikely.

January 16, 1978

CYCLE OF MANAGEMENT PLAN DEVELOPMENT

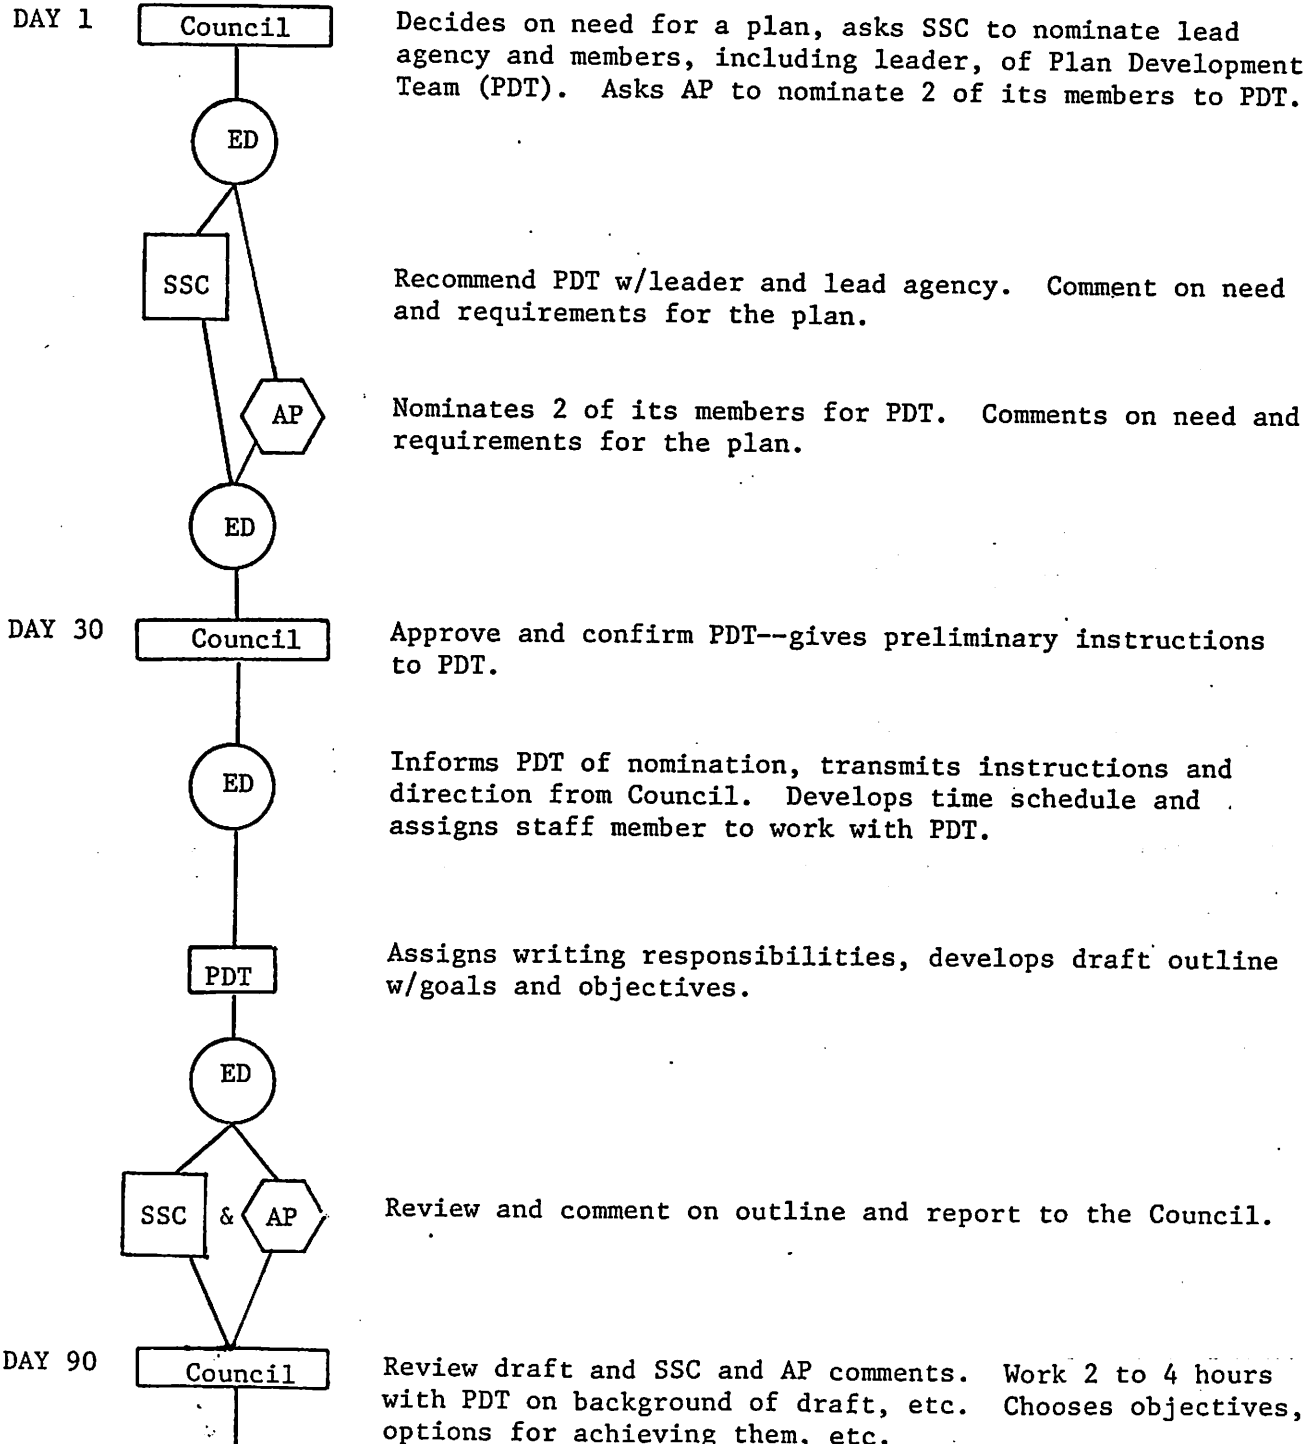



Communicate Council instructions and monitor compliance. Staff member continues work with PDT.




Write draft plan, following Council instructions. Staff member assists with editing, writes DEIS and Summary.




Review and comment on first draft.

DAY 150



Review with SSC and AP -- comment and direct revisions, etc.



Modify and edit as required.



Receives 25 copies to start preliminary review.




Receives copies of DEIS and DFMP plus assurances X number of copies are ready for distribution.



Notice of Availability printed.




Copies mailed for external review.




Holds public hearings in appropriate locations.



Consolidates comments from external review.



Responds to external review if appropriate.

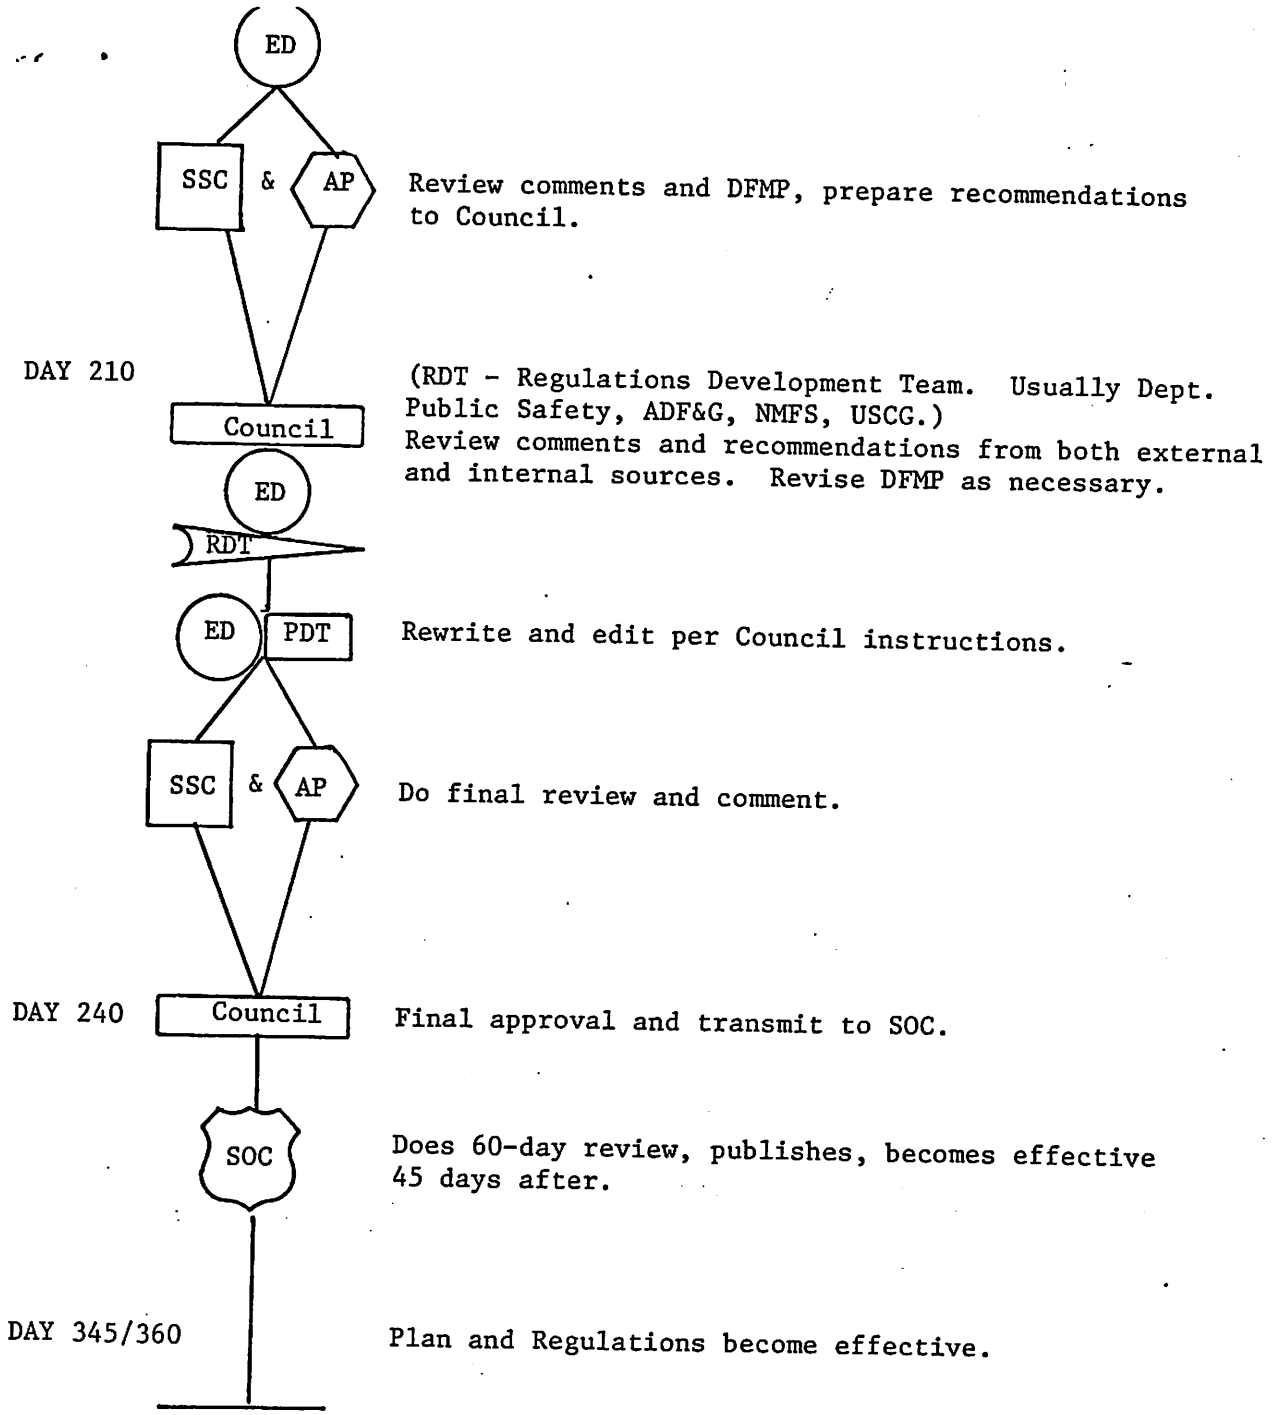

No provision for Economic Impact Statements in this schedule.
